SpaceEye · Strong version (on main)

Local version for review · 4 screens · captured 2026-11-02

Priority map

Whom should the committee visit first?

Visit C18, C07, C14, C03 this cycle (4 of 12 compounds, 2026Q3). C18 comes first: building activity detected; first announced handover date (Dec 2021) passed by 57 months. 2 more at levels 1-3 wait for the next cycle.

To visit this cycle
4 compounds
of 12 · as of 2026Q3

At level 1
1 compound
inspect now · as of 2026Q3

Fine-eligible months
106 months
in 7 compounds · the contract decides the fine · as of 2026Q3

Promised dates ahead
2 dates
in 2 compounds · as of 2026Q3

This cycle's visits



1 · C18 Inspect now
building activity detected; first announced handover date (Dec 2021) passed by 57 months
Wayback capture 2025-07-23



2 · C07 Inspect this cycle
no building activity for 2 quarters; no announced handover date
Wayback capture 2025-07-23



3 · C14 Inspect this cycle
building activity detected; first announced handover date (Dec 2024) passed by 21 months
Wayback capture 2025-07-23



4 · C03 Document review
no building activity for 6 quarters; handover announced; may be complete (handover announced): confirm on site
Wayback capture 2025-07-23

Priority map

Wayback capture 2025-07-23

SpaceEye
R7 · Observatory

Data track

Track A: images

Screens

- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED

Priority map



Inspect now · 1 | Inspect this cycle · 2 | Document review · 3 | Routine · 6 | Not assessable · 0

derived · as of 2026Q3 · colour = priority level, grey = not assessable · block height = mean building height (Google Open Buildings, latest year to 2024), drawn 10× taller · right-drag to tilt or turn

Visit list

Suggested actions are proposals; the committee decides.

Rank	Compound	Level	Suggested action	Why

Track A · screen 1 · part 2

10× taller · right-drag to tilt or turn

SpaceEye
R7 · Observatory

Data track
Track A: images

Screens
1 · Priority map
2 · Compound file
3 · District view
4 · Scenarios

REAL · DERIVED

Visit list

Suggested actions are proposals; the committee decides.

Rank	Compound	Level	Suggested action	Why
1	C18	Inspect now	Fine review	building activity detected; first announced handover date (Dec 2021) pass
2	C07	Inspect this cycle	Visit this cycle	no building activity for 2 quarters; no announced handover date
3	C14	Inspect this cycle	Written warning	building activity detected; first announced handover date (Dec 2024) pass
4	C03	Document review	Confirm handover on site	no building activity for 6 quarters; handover announced; may be complet

Cycle list (CSV)

Changes since 2026Q2

Joined the list

C07 · level 3 to 2
no building activity for 2 quarters; no announced handover date

Left the list

C10 · level 1 to 4
building activity detected; handover announced; may be complete (handover announced): confirm on site

Promised dates ahead

A visit before these dates can check the developer's own promise.

Compound	Promise	Said in	Due by
C14	promised handover in 2027	Feb 2026	2027-12-31
C21	promised handover by Dec 2027	Feb 2026	2027-12-31

SpaceEye
R7 · Observatory

Data track
Track A: images

Screens
- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED

Compound file

Why this one? Evidence behind the priority level.

Compound
C18 · Inspect now

Level 1 · Inspect now. Suggested action: **Fine review.** 45 fine-eligible months (proposal: 12). Last recorded visit: no visit recorded yet.

The action is a suggestion; the committee decides.

Why: building activity detected; first announced handover date (Dec 2021) passed by 57 months

Indicators

Priority level
Inspect now
worst of K2, K3, K6 · as of 2026Q3

K2 no activity
0 quarter(s)
counted after the start: 4 active quarters or a published launch · as of 2026Q3

K3 handover clock
57 months
since first announced handover date · as of 2026Q3

K6 never started
does not apply
construction start was observed · as of 2026Q3

K5 fine-eligible months
45 months
the contract decides the fine · as of 2026Q3

Level history



Inspect now · Inspect this cycle · Document review · Routine · Not assessable

Satellite curves

Track A · screen 2 · part 1

Inspect now · Inspect this cycle · Document review · Routine · Not assessable

Satellite curves



📌 **First announced handover date:** Dec 2021 (the date K3 counts from)

derived · gaps = quarters not assessable · dashed lines = quarter of a published developer statement

Construction stage by year



land or ground works · under construction · complete

Construction first seen in 2020.

Wayback timeline

Capture date

SpaceEye
R7 · Observatory

Data track

Track A: images

Screens

- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED

Wayback timeline

Capture date

2025-07-23

C18 | capture 2025-07-23



Wayback release 2026-09-24 | Esri World Imagery Wayback; imagery: Vantor. Service credits: Esri, Vantor, Earthstar Geographics, and the GIS User Community
Cyan: reviewed working boundary, not a legal survey. Source dates may vary within the map.
Static educational report figure. Third-party imagery rights retained; not an open imagery dataset.

Captured
2025-07-23

Stage in 2025
under construction

9 of 9 captures

Compare two captures

Compare: from

Compare: to


Track A · screen 2 · part 3

Cyan: reviewed working boundary, not a legal survey. Source dates may vary within the map.
Static educational report figure. Third-party imagery rights retained; not an open imagery dataset.

Compare two captures

Compare: from
2016-12-17

Compare: to
2025-07-23

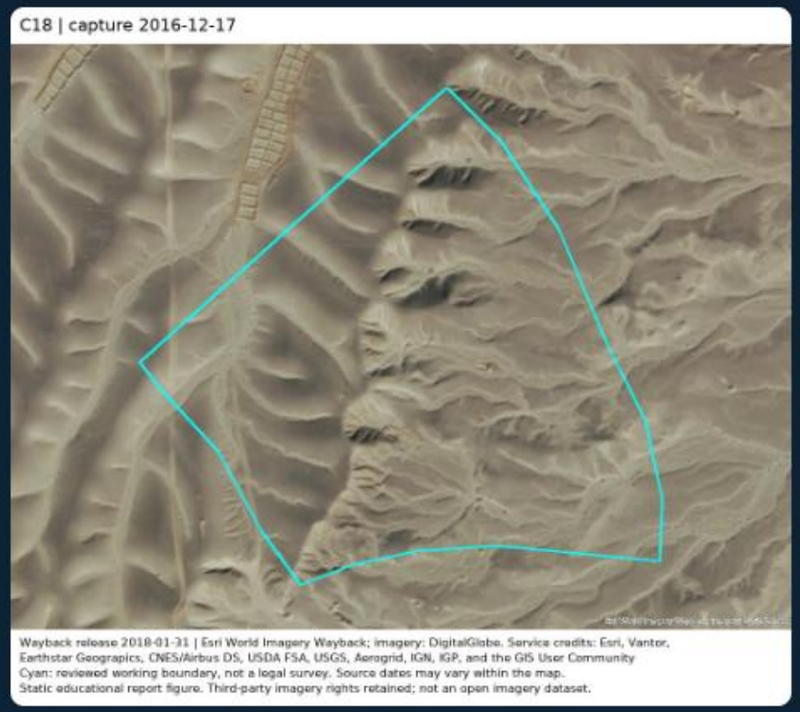

2016-12-17 · land or ground works



2025-07-23 · under construction

Developer claims vs what space showed

Published	Claim	Promised year	Nearest capture
Jul 2021	progress 65%		2021-04-09: under construction
Sep 2021	progress over 70%		2021-04-09: under construction
Sep 2021	promised handover Jun-Jul 2023	2023 passed, space showed under construction	2021-04-09: under construction
Sep 2021	promised phase 1 handover Oct-Dec 2021	2021 passed, space showed under construction	2021-

2016-12-17 · land or ground works

2025-07-23 · under construction

SpaceEye

R7 · Observatory

Data track

Track A: images

Screens

- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED

Developer claims vs what space showed

Published	Claim	Promised year	Nearest capture
Jul 2021	progress 65%		2021-04-09: under construction
Sep 2021	progress over 70%		2021-04-09: under construction
Sep 2021	promised handover Jun-Jul 2023	2023 passed, space showed under construction	2021-04-09: under construction
Sep 2021	promised phase 1 handover Oct-Dec 2021	2021 passed, space showed under construction	2021-04-09: under construction
May 2022	progress about 75%		2022-06-13: under construction

Visit form

Record a visit

Pick the compound code. Do not write compound or developer names in the note.

Code

C18

Date

2026/11/02

Result

progressing

Note

Optional: what was seen on site.

Save visit

Track A · screen 2 · part 5

District view

What does the system give the committee?

An early signal: C21

> **C21** was first flagged in 2020Q3, 39 months before its first handover date (Dec 2023).

What space saw. No building activity for 6 quarters; first announced handover date (Dec 2023) is still ahead; no confirmed observed start for 18 months since the first known launch/promise.

By the freeze date (2023-06-30) it was back at level 4 (Routine).

What happened. Partly handed over late, completion postponed, reported Jan 2026.



First capture after the alert · 2021-04-09 · under construction



Latest · 2025-07-23 · under c

SpaceEye
R7 · Observatory

Data track
Track A: images

Screens
- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED



First capture after the alert · 2021-04-09 · under construction



Latest · 2025-07-23 · under construction

Flagged now, before any handover date passed

C07	Level 2 · Inspect this cycle	no building activity for 2 quarters; no announced handover date	Open C07

The developer said, space saw

> **C18**: as of 2026Q3, 57 months past the first announced handover date (Dec 2021).

Published	Claim	Promised year	Nearest capture
Jul 2021	progress 65%		2021-04-09: under construction
Sep 2021	progress over 70%		2021-04-09: under construction
Sep 2021	promised handover Jun-Jul 2023	2023 passed, space showed under construction	2021-04-09: under construction
Sep 2021	promised phase 1 handover Oct-Dec 2021	2021 passed, space showed under construction	2021-04-09: under construction
May 2022	progress about 75%		2022-06-13: under construction

C18 | capture 2022-06-13



C18 | capture 2025-07-23



Track A · screen 3 · part 2

SpaceEye
R7 · Observatory

Data track

Track A: images

Screens

- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED



Nearest to the last claim · 2022-06-13 · under construction



Latest · 2025-07-23 · under construction

Homes in compounds with fine-eligible months

9,937 homes in 7 compounds with fine-eligible months.



Label = fine-eligible months of the compound.

How late R7 promises ran

Track A · screen 3 · part 3

SpaceEye
R7 · Observatory


Data track
Track A: images

Screens
- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED

How late R7 promises ran

Five R7 compounds began handing over 18-33 months after the promised date (median 25).

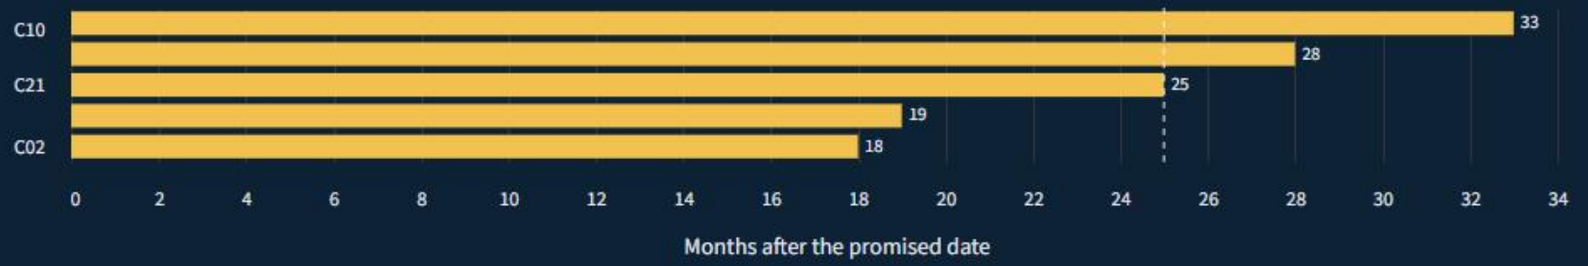

C14: handover postponed twice, not yet delivered.

Dashed line = median.

Fine-eligible months

106 fine-eligible months over 7 compounds today.



The contract decides the fine.



The contract decides the fine.

SpaceEye
R7 · Observatory

Data track

Track A: images

Screens


- 1 · Priority map
- 2 · Compound file
- 3 · District view
- 4 · Scenarios

REAL · DERIVED

Developers with several compounds

D14	C18 · Level 1 · Inspect now	C01 · Level 4 · Routine	
D13	C14 · Level 2 · Inspect this cycle	C21 · Level 3 · Document review	
D12	C12 · Level 3 · Document review	C04 · Level 4 · Routine	C10 · Level 4 · Routine

Level history, all compounds

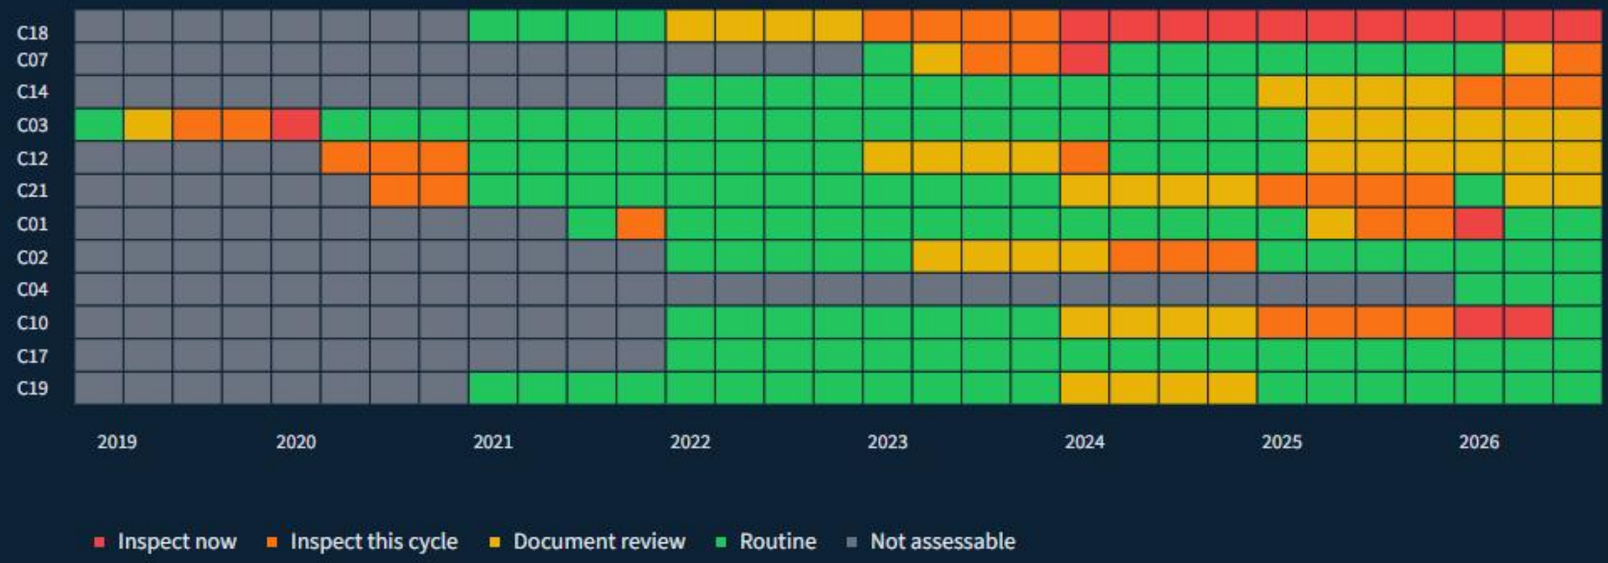

Synthetic - for training only

Scenarios

Who would change if costs, collections or visit capacity changed?

S1 · Cost shock | S2 · Collections drop | S3 · Capacity

Generated · Imported cost +30%. · 2026-09

Nobody crosses a threshold: no compound changes level or list position.
